



John Booth Arboricultural Consultants Ltd
*John A Booth MBA, MSc, CEnv, FArborA, RArborA,
DipArb(RFS), CUEW, LCGI(Hort), NDArb.*
Director & Principal Consultant
Chartered Environmentalist, Certificated Expert Witness
& Arboricultural Association Registered Consultant

Arboricultural Survey Report & Method Statement

at

**Foxes Low Road
Spalding
PE12 7PA**

for and on behalf of

Purewal Developments Ltd

10 June 2026

**242 Highfields Park Drive
Broadway
Derby
DE22 1JY**

**Mobile: 07783 968714
Email: info@jabooth.co.uk
Web: www.jabooth.co.uk**



SUMMARY

This report concerns trees located on land at Foxes Low Road, Spalding, PE12 7PA; it is concerned with a proposal to develop the site.

The report and accompanying tree survey schedule is produced in accordance with the guiding principles of British Standard 5837:2012 '*Trees in Relation to Design, Demolition and Construction – Recommendations*'.

The Root Protection Area (RPA) of the trees surveyed are calculated and recorded in the Tree Survey Schedule where they are expressed both in linear and square metres; it is at this distance/around this area that tree protective barriers should be erected around any trees to be retained.

The site is heavily vegetated, limiting access; dimensions are estimated.

The findings of my survey are that whilst the proposal does necessitate the loss of trees, none are of any great merit and compensatory planting is proposed.

All rights in this report are reserved. Its content and format are for the exclusive use of the addressee and agents in dealing with the subject matter and only they may reproduce or transmit it, in any form or by any means, electronic, mechanical, photocopying, recording or otherwise. It may not be sold, lent, hired out or divulged to any third party not directly involved in the matter concerned without the written consent of John Booth Arboricultural Consultants Ltd.

©John Booth Ltd 2026

Contents

1	Introduction
	1.1 Author's Qualifications and Experience
	1.2 Instructions & Brief
	1.3 Documents and Information Provided
	1.4 Scope
2	Site Visit and Observations
	2.1 Site Visit
	2.2 Tree Survey Methodology
3	Other Considerations
	3.1 Trees Subject to Statutory Controls
	3.2 Trees and Wildlife
	3.3 Implementation of Tree Works
4	Conclusions
5	Bibliography
6	Tree Survey Schedule & Plan
7	Appendices
	Appendix 1 Tree Survey Methodology

Figures

1	Location Plan
----------	---------------

1 INTRODUCTION

1.1 Author's Qualifications and Experience: I am a Chartered Environmentalist, a Fellow and Registered Consultant of the Arboricultural Association; I am also a past national chairman of the Arboricultural Association. I have many years' experience of arboriculture and amenity tree management and have written papers published in respected journals such as the International Journal of Urban Forestry and was a member of drafting group responsible for the writing of the National Tree Safety Groups publication '*Common sense management of trees*'. I am trained in the use of the Quantified Tree Risk Assessment (QTRA) methodology and am a Bond Solon/Cardiff University certificated Expert Witness.

This report is based on my site observations and the information provided.

For your assurance I carry £5,000,000.00 Professional Indemnity insurance.

This report is based on my site observations and any information provided.

1.2 Instructions and Brief: Purewal Developments Ltd (my client) sought advice regarding the condition of trees which might be implicated in a proposal to develop a site on land Foxes Low Road, Spalding, PE12 7PA (the site). Guidance was sought as to what arboricultural constraints might be associated with the proposal and how any such might be overcome/minimised. A Tree Survey Schedule compliant with the guiding principles of British Standard 5837:2012 '*Trees in Relation to Design, Demolition and Construction – Recommendations*' is contained in this report, and all survey data is recorded in this Schedule.

1.3 Documents & Information Provided: plans illustrating the existing and proposed layouts were provided; the former has been annotated and supplements the accompanying Tree Survey Schedule.

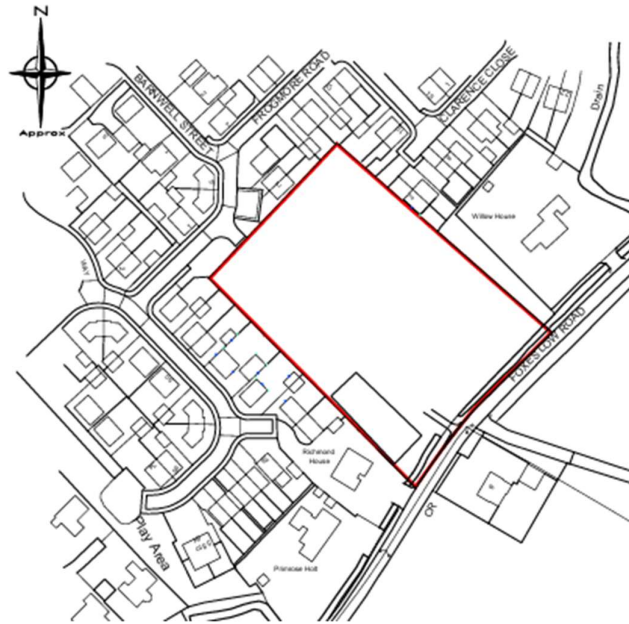


Fig 1 Location Plan

1.4 Scope:

1.4.1 This report has been prepared for the sole use of the client. Any third party referring to this report or relying on the information contained herein does so entirely at his or her own risk.

1.4.2 Whilst every effort has been made to detect defects within the subject trees, no guarantee can be given as to the absolute safety or otherwise of any individual tree. This report represents a survey and should not be construed to be a detailed tree inspection report; trees comprising groups were assessed as such and individuals within were not subject to inspection. Any recommendations given are intended to reduce the likelihood of tree collapse and are intended to reduce the likelihood of tree collapse but absolute safety is not a realistic goal; even apparently sound trees can fail particularly during inclement weather eg Gale force winds of 8 (39 - 46 mph) may result in the shedding of small twigs and branches whereas Gale force 10 winds (55 – 63 mph) may result in trees being uprooted. All recommendations are given in the context of the site's current usage; any change will dictate a further survey.

1.4.3 The findings and recommendations contained within this report are, assuming its recommendations are observed, valid for a period of twelve months from the date of survey. Trees are living organisms subject to change – best practice dictates they are inspected on a regular basis for reasons of safety.

1.4.4 My expertise is ARBORICULTURE, any non-arboricultural references made within this report are made as a lay person.

2 SITE VISIT AND OBSERVATIONS

2.1 Site Visit: I undertook a site visit on 10 June 2026. The trees were surveyed visually from the ground. No drilling or excavation was carried out on this occasion. The weather at the time of the visit was dry and still, visibility was adequate for the purposes of the visit.

2.2 Tree Survey Methodology: The survey was undertaken in accordance with the guiding principles of British Standard 5837:2012 '*Trees in Relation to Design, Demolition and Construction – Recommendations*' (BS5837) and the trees were assessed objectively and without reference or influence being given to any proposed site layout. Using 'Visual Tree Assessment' (VTA) techniques the trees were surveyed from the ground. VTA is a methodology, employed by arboriculturists, to evaluate the structural integrity of a tree, relying on observation of a tree's biomechanical and physiological features; this is the method generally adopted and is appropriate in this instance. Groups of trees would be identified as such in instances as are defined in BS 5837 (2012) ie where, by virtue of the fact that trees are in such proximity they function as a unit, in visual terms, aerodynamically or culturally. Any shrubs and insignificant trees were omitted from the survey.

Further explanatory details regarding the survey methodology can be found at Appendix 1.

3 OTHER CONSIDERATIONS

3.1 *Trees Subject to Statutory Controls:* No attempt has been made to establish the existence of any statutory controls; the following is given as guidance.

3.1.1 Trees and hedgerows can be subject to statutory control, and severe penalties can result from unauthorised works or damage. It is recommended that prior to commencement of any tree works the Local Planning Authority (LPA) are contacted. When proposing to do works to trees within a Conservation Area, with some exceptions, eg the implementation of works directly necessary to implement a full planning permission, six weeks written notice must be given to the LPA, this notice need not take any form other than a written specification of what is proposed and a plan illustrating the position of the tree(s). This notice is often referred to as a Section 211 Notice. Many LPAs prefer that their standard pro-forma is submitted to ensure the necessary detail is included in the notice; whilst such cannot be strictly required it can assist in a speedy outcome.

3.1.2 Having received the notice, the LPA has essentially only one of two options at its disposal ie:

- **Impose a TPO** in respect of those trees/some of those trees subject to the notice. This prevents any works being carried out without the express, written consent of the LPA,
Or
- **Do nothing** It is considered best practice for an LPA to acknowledge receipt of the notice but there is no obligation for it to do so. After six weeks of serving the notice the tree owner may proceed with the works detailed in the Section 211 Notice.

3.1.3 The LPA cannot, in response to a Section 211 Notice, issue a conditional consent.

3.1.4 TPO's are made in the interests of preserving amenity, usually taken to mean public visual amenity. Trees largely removed from public view, and which have little visual impact are not usually made the subject of a TPO. The written consent of the LPA must be obtained prior to undertaking works to trees subject to TPO unless, as with trees in Conservation Areas, certain exemptions apply.

3.1.5 Regarding trees subject to TPO's it is a requirement that a standardized application form is used; this form is available from the LPA.

3.2 *Trees and Wildlife:* Trees play host to nesting birds all of which are protected by law. All British bat species are also protected and can be found in trees. Great care needs to be taken to avoid disturbance, and consideration should be given to the timing of tree works to avoid disturbance. Where the presence of protected species is suspected, Natural England should be contacted for advice.

3.3 *Implementation of Tree Works:* Guidance on hiring an Arborist is available from the Arboricultural Association's Register of Contractors, which is available free from Ullenwood Court, Ullenwood, Cheltenham, Gloucestershire, GL53 9QS (Telephone 01242 522152, www.trees.org.uk). Any appointed contractor should carry out all tree works to BS 3998 (2010) '*Recommendations for Tree Work.*'

4 CONCLUSIONS

4.1 The site is heavily vegetated, limiting access; dimensions are estimated.

4.2 The findings of my survey are that whilst the proposal does necessitate the loss of trees, none are of any great merit and compensatory planting is proposed.

5 BIBLIOGRAPHY

- British Standard 5837:2012 '*Trees in Relation to Design, Demolition and Construction – Recommendations*'. BSI.
- British Standard 3998:2010 '*Recommendations for Tree Work*'. BSI.
- Mattheck, C., (2007), '*Updated Field Guide for Visual Tree Assessment*'.

**John A Booth MBA, MSc, CEnv, FArborA, RCarborA, DipArb(RFS), CUEW, LCGI(Hort),
NDArb.**
**Chartered Environmentalist, Certificated Expert Witness & Arboricultural
Association Registered Consultant**


6 Tree Survey Schedule (Explanatory Notes Found at Appendix 1)

Tree No	Species	Ht (m)	Stem Dia (mm)	Branch Spread (m)				Crown Ht. (m)	Age Class	Cond	Comments/ Preliminary Recs.	Life Exp (yrs)	Ret Cat	RPA* (Lin M)	RPA** (M ²)
				N	E	S	W								
G1	Goat willow	9 (12)	400	5	5	5	5	2	Mat	B	Remove to facilitate proposal.	10-20	C	-	-
1	Crab apple	7 (9)	350	4	4	4	4	2	Mat	B	Remove to facilitate proposal.	10-20	C	-	-
G2	Privet	3 (5)	<150	2	2	2	2	0	Mid	B	Remove to facilitate proposal.	10-20	C	-	-
G3	Cherry, Hawthorn	4 (12)	300	3	3	3	3	02	Mid	B	Remove to facilitate proposal.	>40	C	-	-

* RPA =The minimum distance, measured from the tree's trunk, at which tree protective barriers should usually be erected.

** RPA =The minimum area in M² around which tree protective barriers should usually be erected.

6.1 Tree Survey Plan (Indicative)

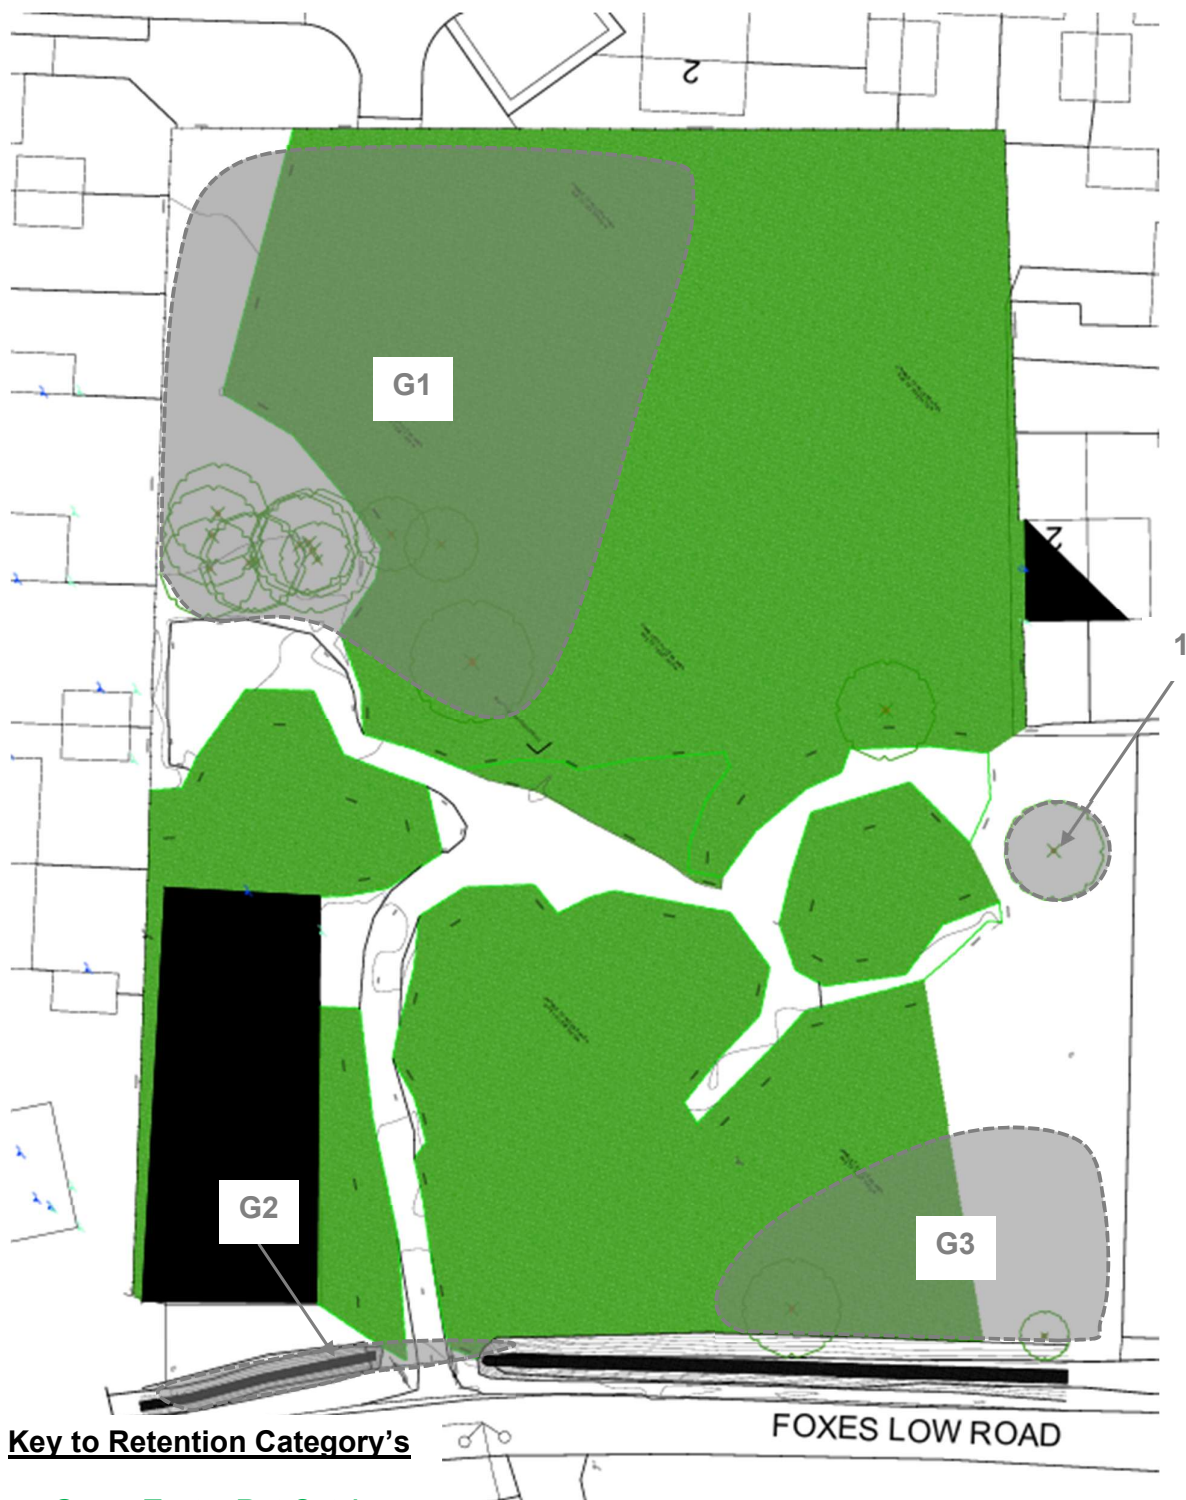

7 APPENDICES

Appendix 1: Tree Survey Methodology

The survey was undertaken in accordance with the guiding principles of BS5837. Significant trees omitted from the plan provided were plotted by eye and included within the survey. Information recorded in the survey includes:

Species – the species identification is based on visual observations and the common English name of what the tree appeared to be is listed. In the case of groups only the principal species are recorded, other minor species may be omitted.

Tree Heights – are estimated in metres. Estimated mature heights are given in brackets. In the case of groups, the mean current height is recorded.

Crown Height – the height to the lowest branch is estimated in metres. In the case of groups of trees minimum crown height was recorded.

Trunk Diameters – measured at 1.5 metres above ground and recorded in millimetres to the nearest 10mm. However, in accordance with BS5837 where the trunk of any tree breaks below 1.5 metres it is considered a multi-stemmed tree. In the case of groups of trees, the maximum diameter was recorded.

Crown Radius – was recorded in metres along each of the cardinal points. In the case of groups of trees, the maximum peripheral spread was recorded.

Crown Height – height from ground level to lowest principal limb.

Age Class – recorded as follows:

- Yng - Young tree; <1/3 of normal life expectancy
- Mid - Middle aged tree; between 1/3 & 2/3 normal life expectancy
- Mat - Mature tree; has attained optimum stature
- OM - Over Mature tree; declining

Vet - Veteran tree; tree of great age which is of exceptional value culturally, in the landscape or for nature conservation.

The **Condition** of the trees is based upon a preliminary assessment categorised thus:

- A - Good
- B - Fair
- C - Poor
- D - Very Poor/Dead

In the case of groups, the category awarded is that typical of the group.

Preliminary Recommendations – works required regardless of development proposals.

Life Expectancy – estimated; ie less than 10 years, 10-20 years, 20-40 years, more than 40 years.

A **Retention Category** is given as follows which corresponds with Table 1 of BS 5837' ie:

- **A** - Trees of a high quality and value, including public visual amenity value. It is usual for such trees to be retained unless the planning merits of a particular scheme or layout over-ride.
- **B** - Trees of moderate quality and value, including public visual amenity value. Such trees should be considered for retention.
- **C** - Trees with a stem diameter of less than 150mm or which are of low quality/value, including public visual amenity value and/or have and life expectancy of less than 10 years value. **The retention of Category C trees should not be allowed to impose a constraint on development.** Trees with a stem diameter of less than 150mm are classified as Retention Category C, they should be considered for transplanting.
- **U** - Trees in such a condition that they are unsuitable for retention. Where category U trees have identifiable conservation, heritage or landscape value, even though only for

the short term (less than 10 years), they may be retained where they are (or can be) sited such that concerns over safety are at (or can be reduced to) acceptable levels.

It must be noted that Retention Categories are awarded purely on arboricultural/amenity grounds and that in some instances the planning merits of a particular scheme may well over-ride the retention of even those trees qualifying for Retention Category 'A'.

Root Protection Area (RPA) – In respect of all trees surveyed the RPA has been calculated and is given in the Tree Survey Schedule. The figures given represent both the radial distance, from the tree's trunk, at which the barriers should be erected and the entire area which should be encompassed by the barriers.



John Booth Arboricultural Consultants Ltd
John A Booth MBA, MSc, CEnv, FArborA, RCarborA,
DipArb(RFS), CUEW, LCGI(Hort), NDArb.
Director & Principal Consultant
Chartered Environmentalist, Certificated Expert Witness
& Arboricultural Association Registered Consultant

242 Highfields Park Drive
Broadway
Derby
DE22 1JY

Mobile: 07783 968714
Email: info@jabooth.co.uk
Web: www.jabooth.co.uk

