
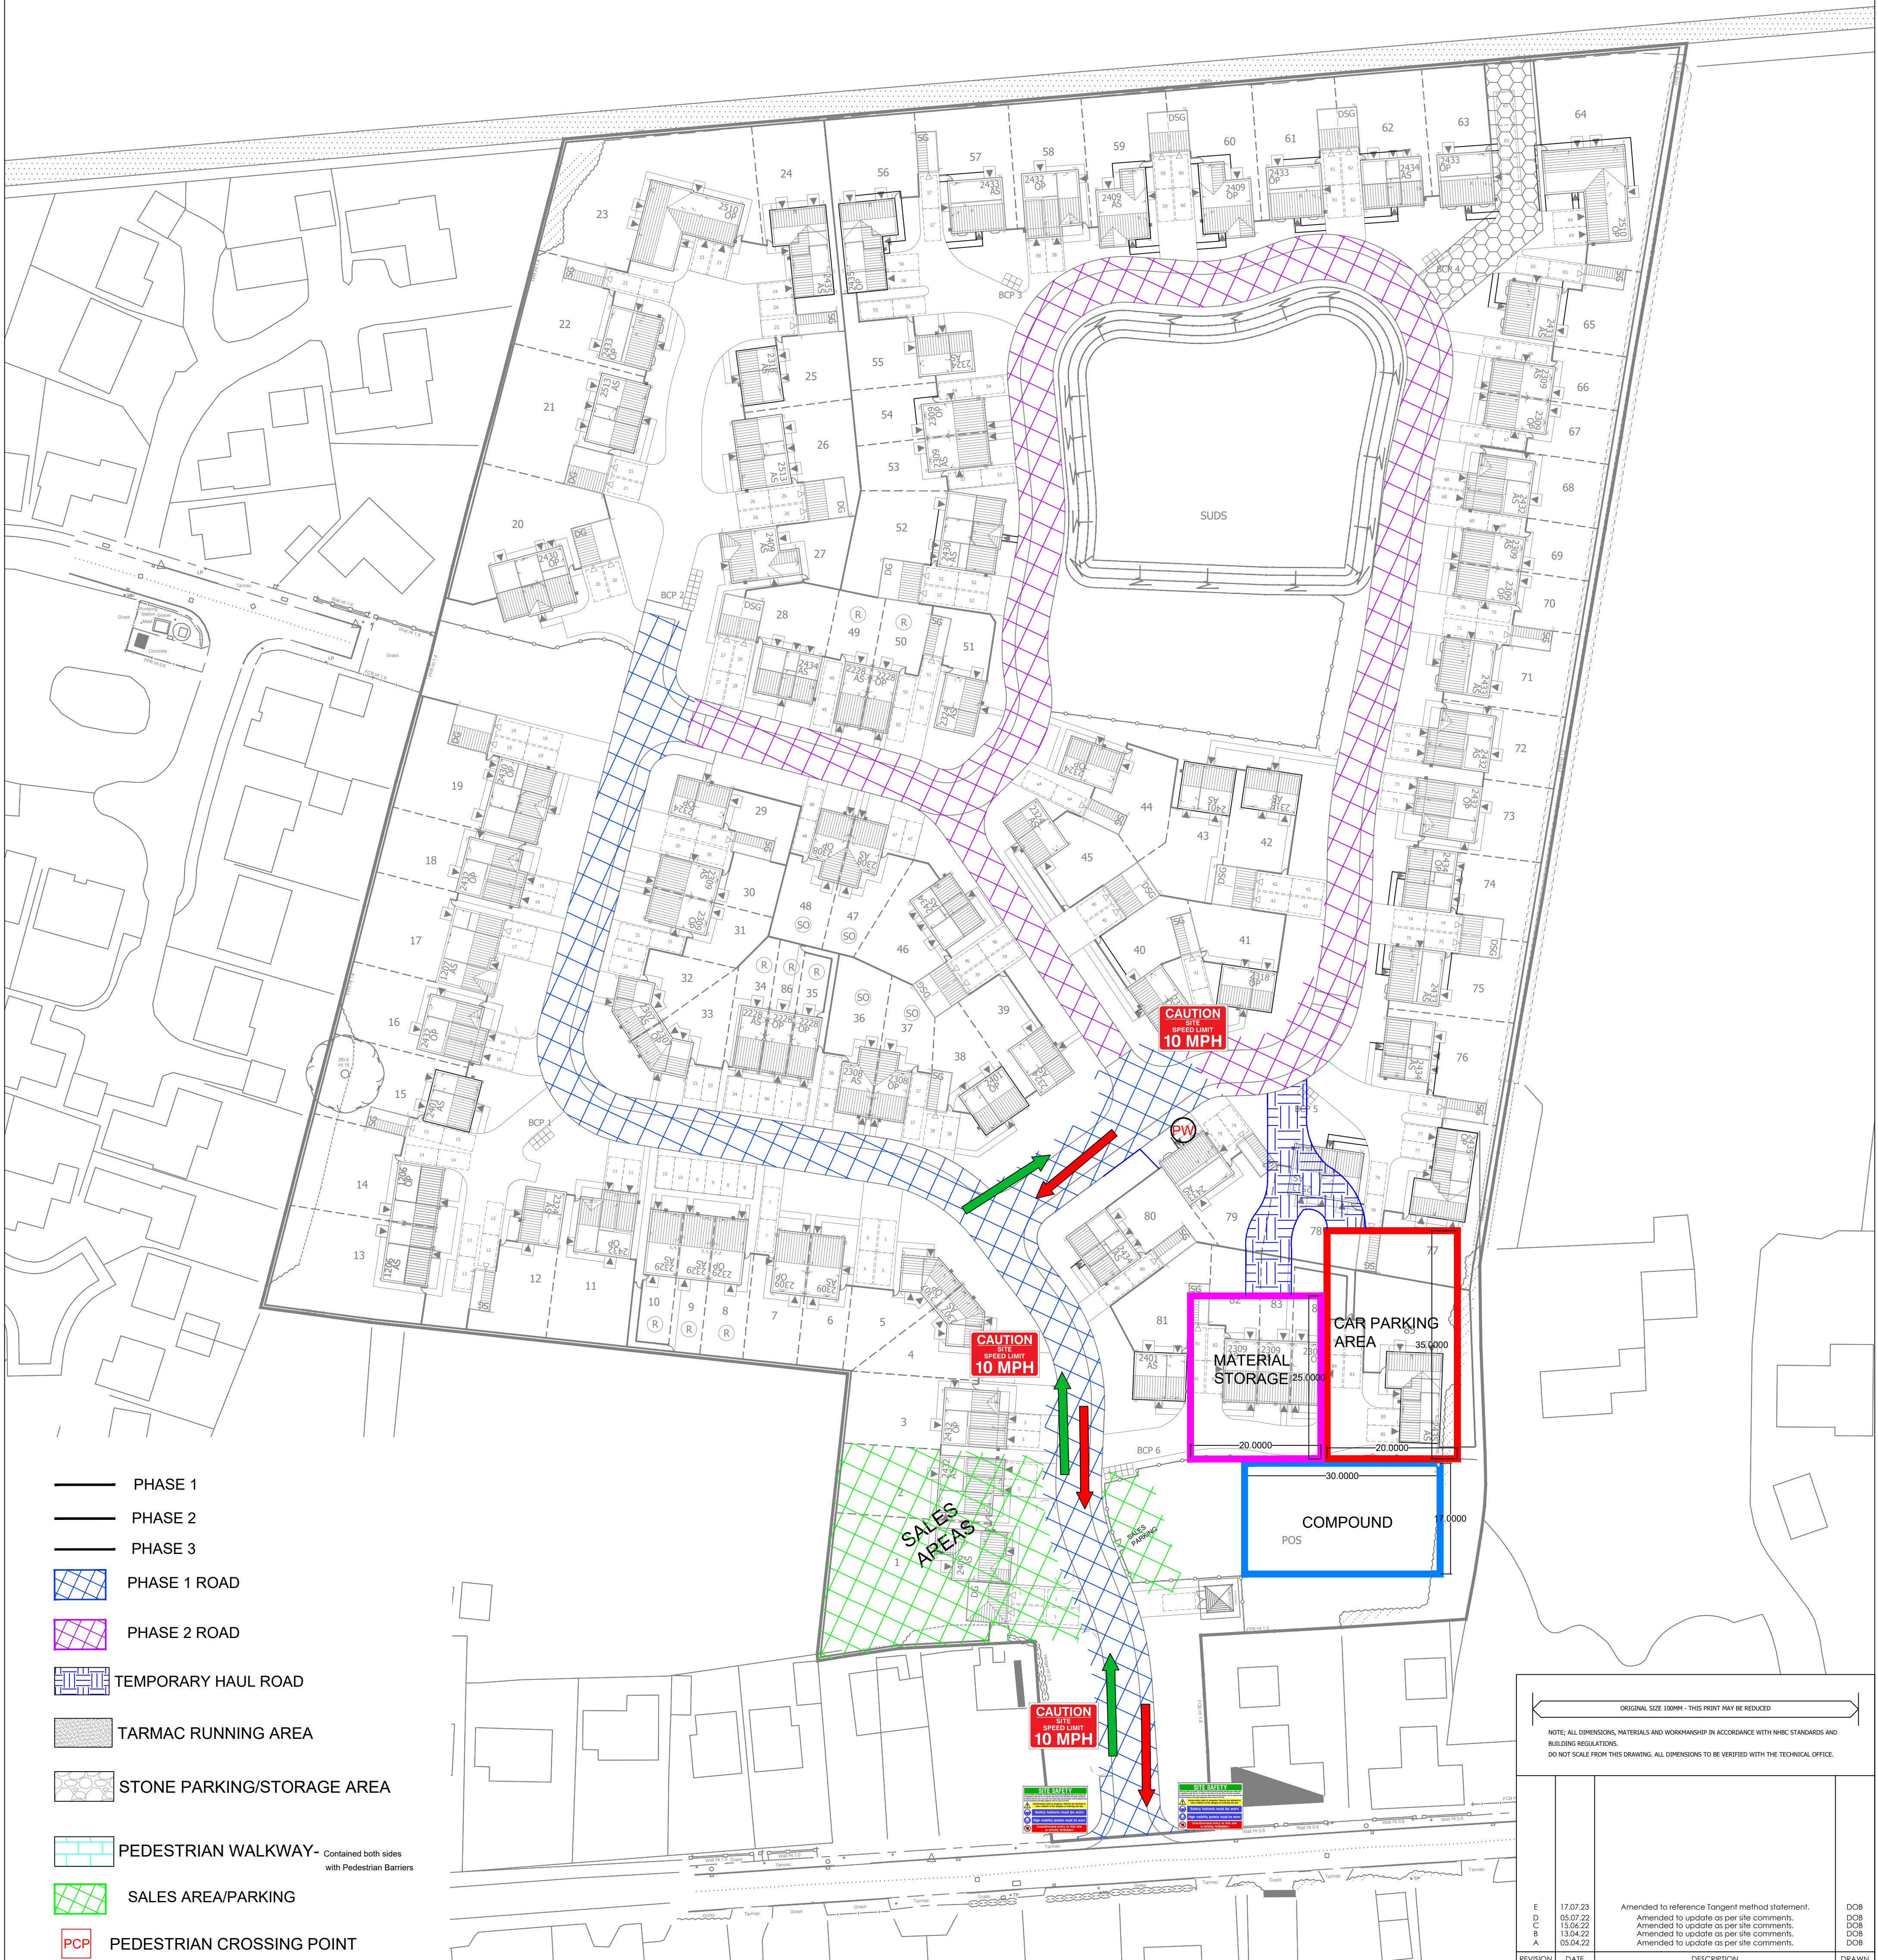




- PHASE 1
- PHASE 2
- PHASE 3
- PHASE 1 ROAD
- PHASE 2 ROAD
- TEMPORARY HAUL ROAD
- TARMAC RUNNING AREA
- STONE PARKING/STORAGE AREA
- PEDESTRIAN WALKWAY - Contained both sides with Pedestrian Barriers
- SALES AREA/PARKING
- PEDESTRIAN CROSSING POINT
- 10MPH SITE SPEED LIMIT SIGN
- FIRST AID POINT
- SITE H&S SIGNAGE
- SITE TRAFFIC ROUTE
- COMPOUND FENCING
- HERAS FENCING
- POST & RAIL FENCE
- HOARDING FENCING

**Control of dust**

DRIVE THROUGH WHEEL WASH STATION

A Tornado D1ES Cold water pressure washer and bowser (diesel) will be used on all construction vehicles leaving the site.

**Noise Management**

The site manager shall monitor noise pollution across their site at all times.

Where practically possible, quiet equipment shall be used. Machinery and equipment should only be used for the required time.

Vehicles shall not be revved and engines shall not be left running when not required to be in operation.

Where dust issues are likely to occur, for example when cutting and excavating, dust suppression and use of RPE (respiratory protection equipment), and where appropriate wetting practices should be implemented.

The condition of site haul routes shall be monitored. Mud is not to be taken onto public roads. Road sweeping and road wetting to be implemented as required.

**NOTE: TO BE READ IN CORRELATION WITH TANGENT GROUP REMEDIATION METHOD STATEMENT**

**SITE WORKING HOURS**

To be 7.30am - 5.00pm Monday to Friday, Saturday 8.30am - 1.00pm. No Sunday or Bank Holiday working.

Materials suppliers are to be instructed not to arrive to site prior 7.30am to avoid disturbance to neighbours or potential highway obstruction.

**Light pollution management**

The use of externally facing lighting is not envisaged. Site manager to monitor for change and review.

**Silt Trap**

Silt Trap measures to be in place to prevent contamination of watercourses.

**Complaints Procedure**

The site managers details are provided on site. Alternative contact to be made direct to Larkfleet Homes Head Office, the site manager will be alerted and any necessary action will be taken.

**SITE MANAGER: TBC**  
**PHONE NUMBER: TBC**  
**HEAD OFFICE: 01778 391550**

ORIGINAL SIZE 1000MM - THIS PRINT MAY BE REDUCED

NOTE: ALL DIMENSIONS, MATERIALS AND WORKMANSHIP IN ACCORDANCE WITH NHBC STANDARDS AND BUILDING REGULATIONS. DO NOT SCALE FROM THIS DRAWING. ALL DIMENSIONS TO BE VERIFIED WITH THE TECHNICAL OFFICE.

| E        | 17.07.23 | Amended to reference Tangent method statement. | DOB   |
|----------|----------|------------------------------------------------|-------|
| D        | 05.07.22 | Amended to update as per site comments.        | DOB   |
| C        | 13.04.22 | Amended to update as per site comments.        | DOB   |
| B        | 05.04.22 | Amended to update as per site comments.        | DOB   |
| A        |          |                                                |       |
| REVISION | DATE     | DESCRIPTION                                    | DRAWN |

LARKFLEET HOMES  
LARKFLEET HOUSE  
SOUTHFIELDS BUSINESS PARK  
BOURNE  
LINCOLNSHIRE  
PE10 0FF  
TEL: 01778 391550

PROJECT

ROMAN ROAD  
MOULTON CHAPEL

DRAWING TITLE

CONSTRUCTION  
MANAGEMENT PLAN

|             |            |       |          |
|-------------|------------|-------|----------|
| SCALE       | DATE       | DRAWN | APPROVED |
| 1:500 @ A1  | 27.05.2021 | DOB   | -        |
| DRAWING NO. |            |       | REVISION |
| L181/CMP/01 |            |       | E        |
