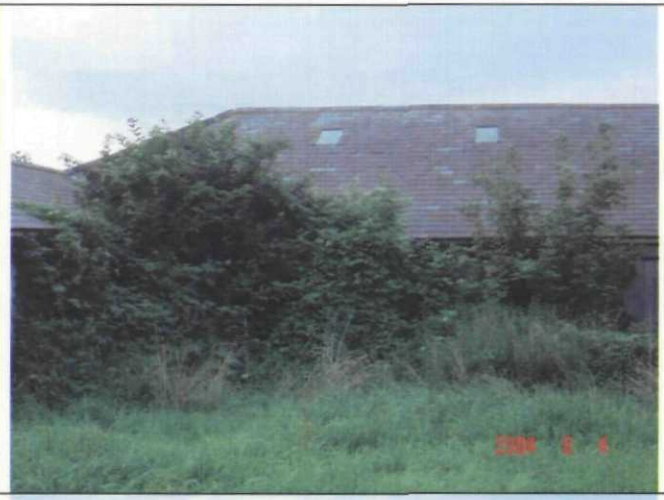
50	Open area	Trees/bushes	Remove and dig trial hole to asses damage to adjacent foundations.	
51	Gable detail Open Area	Heavy cracking and associated movement possibly caused by failed valley detail. Internal evidence of past roof failure i.e. brick/mortar damaged and propped roof rafters and joists.	Strip out damaged timber and replace with re – claimed timber or new seasoned timber of same type.	
