

plandescil
consulting engineers

Telephone: (01953) 452001 / Fax: (01953) 456955

APPENDIX 1



location plan

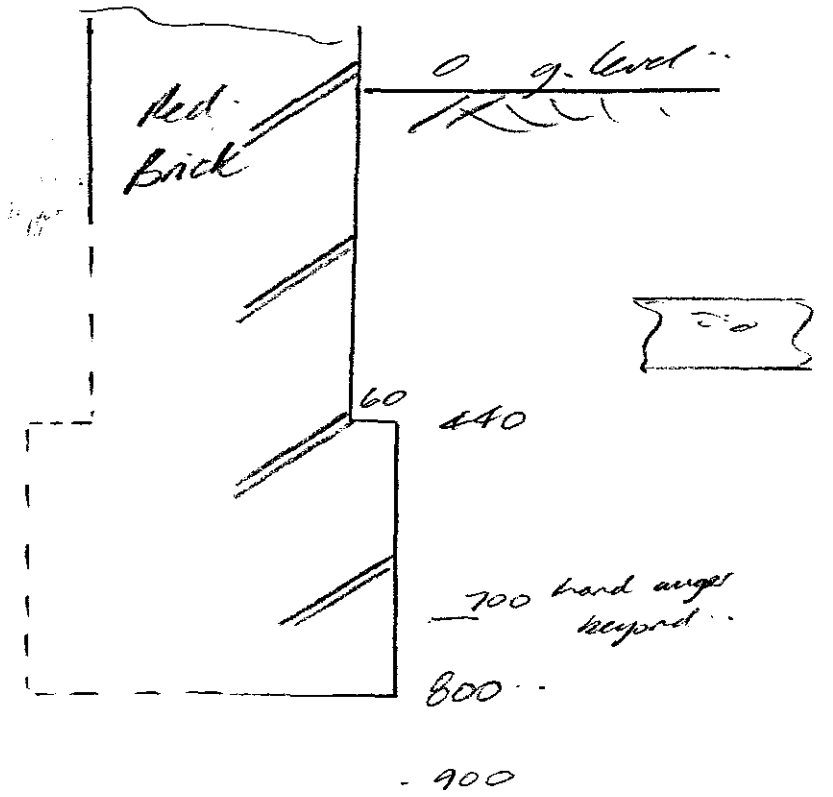

gravel

concrete slabs (broken down)

Brown silt with brick fragment

Beyond wall base brown silts with stone content. Unable to retrieve core as fell through auger

TRIAL HOLE on WALL BASE.

Note:

Gravel at high level over concrete slab tended to fall into hole as excavation proceeded. Augering tended to 'catch' side of brick footing and obviously infill at higher level. Entirely 'clean' virgin subsoil was not noted prior to core retrieval proving impossible. See borehole 3 just to north showed natural clayey silt beyond 550mm.

Job No: 10242
